NAROLA INFOTECH

Greenfield multi-tenant textile manufacturing operations SAAS

Raj Patel

Prepared By:

Urvesh Sojitra
(Business Representative)

Vrushal Meruliya
(Technical Representative)

Comprehensive Project Scope Analysis

1. Executive Summary

Narola Infotech proposes a greenfield, production-ready SaaS implementation designed for Indian grey-fabric weaving factories and engineered around transactional integrity, tenant isolation, traceability, and operational usability.

Our commercial recommendation is to treat Option A as a standalone marketable Estimator SaaS and Option B as the complete connected operating platform. The estimates below include normal production-delivery activities and a realistic contingency for business-rule refinement during discovery.

2. Our Understanding of Weavly

- Reliable textile costing, quote generation and immutable commercial snapshots.
- Party-backed order production and speculative market / make-to-stock production.
- Loom and worker assignment, day/night shift logging, production pace and deadline visibility.
- Godown stock, takas with actual metre quantities, partial sales, dispatch and receipt variance reconciliation.
- Receivables, collections, expected and realised gross profit, meter-worker and fixed-worker payroll, and Upaad / advances.
- SaaS subscription states, Razorpay integration, optional referral tracking and WhatsApp operational messaging.
- Strict tenant isolation, auditable corrections, retry-safe writes, idempotent integrations, backups, monitoring and handover.

3. Confirmed Planning Assumptions

Planning area	Assumption
Year-one tenant count	Approximately 10-25 factory organisations
Scale target	At least 100 tenants without fundamental rearchitecture
Typical looms per factory	Approximately 12-50
Larger test scenario	Up to approximately 150 looms
Typical workers per factory	Approximately 10-40
Larger worker scenario	Up to approximately 100 workers
Orders / market runs	Approximately 20-60 per factory per month
Production logging	Generally, one entry per active loom per shift, including day/night shifts where applicable
Estimator usage	Approximately 100-500 calculations or saved estimates per factory per month

4. OPTION A - ESTIMATOR PRODUCT

A standalone, commercially deployable textile costing and quotation SaaS product - not a single calculator screen.

4.1 Scope Included

- Owner signup, login, password recovery, organisation creation and tenant-scoped access.
- Factory cost-profile wizard with power, labour, loom, fixed/variable overhead and recurring cost assumptions.
- Multiple warp/weft rows, yarn rates, GST inputs, denier/count, ends/picks and row-level deterministic calculations.
- Reed space / finished width, tape length, shortage/wastage, crimp and other agreed textile inputs.
- Loom type, RPM, power usage, shift hours, theoretical and adjusted production assumptions.
- Warping, sizing, winding, weaving wage, processing, finishing and configurable service costs.
- Transport, commission, overhead, margin/profit and tax treatment.
- Cost stack explaining yarn, conversion, processes, overhead, commercial additions and final price.
- Scenario comparison for selected rate, output, cost or margin changes.
- Reusable qualities/templates and quotation history with draft, sent, accepted and rejected statuses.
- Immutable quote snapshots, historical restoration/revision, and professional printable/shareable PDF output.
- Responsive PWA experience, dashboard, backup strategy, error logging, production deployment and formula acceptance testing.

4.2 Textile Formula Responsibility

The client will provide formula definitions, terminology, representative worked examples, and expected outputs. Narola Infotech will implement, validate, test and explain the approved formulas in software. Narola is not responsible for independently inventing or reverse-engineering undisclosed textile formulas.

4.3 Option A Proposed Team and Effort

Role	Seniority	Count	Duration
Project Manager / Business Analyst	Senior	1	6 months
Technical Lead / Solution Architect	Senior	1	6 months
UX/UI Designer	Mid-Senior	1	2 months
Frontend Engineer	Senior	1	4.5 months
Backend Engineer	Senior	1	5 months
QA Engineer	Mid-Senior	1	4 months
DevOps / Cloud Engineer	Senior	1	3 months
Total		7	

4.4 Option A Timeline and Milestones

Milestone	Indicative period	Primary deliverable
A1. Discovery and scope baseline	Weeks 1-3	Validated requirements, assumptions, formula inputs, workflows and acceptance examples
A2. UX/UI and architecture	Weeks 2-6	Information architecture, user flows, responsive designs, data model and technical foundation
A3. Core Estimator implementation	Weeks 5-15	Cost profile, formula engine, saved qualities, scenario handling and core dashboard
A4. Quotes, history and PDF	Weeks 12-18	Snapshots, quote statuses, revision flow and document output
A5. QA, security and performance validation	Weeks 16-22	Automated/manual tests, tenant isolation, formula verification and responsive QA
A6. UAT, launch and handover	Weeks 23-26	UAT fixes, production deployment, documentation and knowledge transfer

4.5 Option A Payment Schedule

Milestone	Payment
Project commencement and discovery kickoff	20%
Scope baseline, UX direction and architecture approval	20%
Core Estimator feature-complete staging release	30%
Quotes, PDF and security/QA milestone	10%
UAT acceptance	10%
Production launch, handover and documentation	10%

4.6 Option A Exclusions

- Production orders, market runs, loom assignments and supervisor production logging.
- Godown stock, taka/lot inventory, dispatch and receipt reconciliation.
- Receivables, collections, payroll, worker advances and full factory analytics.
- Native mobile applications, full statutory accounting, GST return filing, government portal integration, IoT/loom sensors and large-scale historical migration.

5. OPTION B - FULL WEAVLY SUITE

A production-ready multi-tenant operating platform connecting Estimator -> Quote -> Order/Market Run -> Production -> Stock -> Dispatch -> Commercials -> Payroll -> SaaS Billing.

5.1 Functional Scope Included

Option A capabilities

- All functionality included in the standalone Estimator Product.
- Accepted quotes can create active orders, market-mode estimates can create market runs.

Onboarding and master data

- Factory identity, production mode, payroll baseline, machines, workers, godowns, parties and saved qualities.
- Owner-controlled supervisor access and regenerable organisation join codes.

Orders and market runs

- Accepted quote to order with immutable commercial and rate snapshots.
- Party-backed and make-to-stock workflows, loom assignment, progress, pace, deadlines, closure and historical traceability.

Supervisor production logging

- Mobile-first day/night shift workspace, India factory date handling, worker/work selection, readings, meter calculation, bulk submit, idempotency and controlled corrections.

Analytics

- Factory Today, pending logs, order/run health, target progress, pace, deadline risk, machine utilisation/status, trends and worker production.

Godown stock and taka/lot management

- Opening/manual/production-origin stock, actual metre quantity per taka, optional default quality length, partial sales, adjustments, movement history and duplicate prevention.

Dispatch and receipt reconciliation

- Transporter/LR/challan/invoice reference fields, package lines, status workflow, public token tracking, received metres, shortage/extra variance and auditable owner override.

Commercials

- Receivables, credit days, due dates, partial/full collections, operational gross profit and filtered outstanding views.

Payroll and advances

- Meter-worker earnings from approved logs and historical rates, fixed-worker payroll from attendance, adjustments, Upaad/advances, capped deductions, settlements and payslip PDFs.

Billing, referrals and messaging

- Trial/subscription states, Razorpay server-side verification and webhooks, optional referrals, WhatsApp operational messages with non-blocking retries and audit.

Security, operations and handover

- Tenant isolation, audit logging, atomic writes, idempotency, backups, monitoring, QA, deployment, documentation, source code and knowledge transfer.

5.2 Taka-to-Metre Model

- A taka is not treated as a globally fixed metre quantity.
- Each taka can retain its actual metre quantity.
- A fabric quality may optionally define a default or expected taka length.
- Actual quantity can be captured or edited during stock entry or production, subject to audit rules.
- Stock calculations are ultimately based on recorded metre quantities while retaining taka count.
- Partial sale, partial dispatch and remaining metres are supported without losing traceability.

5.3 GST and Tax Handling

- Configurable GST rates.
- HSN/SAC codes where applicable.
- Different tax configurations by relevant item, quality or invoice line.
- Intra-state and inter-state treatment where required.
- Tax-inclusive and tax-exclusive calculations where applicable.

Baseline exclusion: complete statutory accounting, GST return filing, general ledger, Tally replacement and direct government-portal integrations are not included unless separately scoped.

5.4 Option B Proposed Team and Effort

Role	Seniority	Count	Duration
Project Manager / Business Analyst	Senior	1	12 months
Technical Lead / Solution Architect	Senior	1	12 months
UX/UI Designer	Mid-Senior	1	3 months
Frontend Engineers	Senior	2	8 months
Backend Engineers	Senior	2	9 months
QA Engineers	Mid-Senior	2	8 months
DevOps / Cloud Engineer	Senior	1	9 months
Total		10	

5.5 Option B Timeline and Milestones

Milestone	Indicative period	Primary deliverable
B1. Discovery and business-rule baseline	Weeks 1-5	Validated workflows, formula inputs, stock/payroll rules, risk register and acceptance criteria
B2. UX/UI, architecture and tenancy foundation	Weeks 3-10	Responsive design system, data model, auth, roles, tenant isolation and environments
B3. Estimator, qualities and quotes	Weeks 8-18	Option A capabilities integrated into Full Suite
B4. Orders, market runs and loom assignments	Weeks 14-25	Party-backed and make-to-stock production contexts
B5. Production logging and analytics	Weeks 20-32	Supervisor workspace, corrections, Factory Today, pace and utilisation
B6. Stock, sales, dispatch and reconciliation	Weeks 27-39	Taka/lot stock, partial sale, dispatch, public receipt and variance handling
B7. Commercials, payroll and advances	Weeks 34-44	Receivables, collections, gross profit, payroll, Upaad and payslips
B8. Billing, messaging and operational hardening	Weeks 40-47	Razorpay, WhatsApp, observability, backup, rate limits and security hardening
B9. Full-system QA, UAT, pilot and production launch	Weeks 45-52	Acceptance journeys, performance smoke tests, pilot, production handover and warranty start

5.6 Option B Payment Schedule

Milestone	Payment
Project commencement and discovery kickoff	15%
Scope baseline, UX direction and architecture approval	10%
Estimator and core platform staging milestone	15%
Orders, market runs and production milestone	15%
Stock, dispatch and commercials milestone	15%
Payroll, billing, messaging and feature-complete staging	15%
UAT and pilot acceptance	10%

Milestone	Payment
Production launch, source-code handover and documentation	5%

6. OPTION C - OPTIONAL FUTURE MODULES

Optional future modules extending the Full Weavly Suite into deeper ERP, inventory, accounting, governance, analytics, native mobile and connected-factory capabilities.

6.1 Functional Scope Included

Yarn inventory and beam management

- Yarn inventory, yarn lots, opening stock, inward, movements, adjustments and stock availability.
- Beam cards, yarn allocation, loom linkage and movement history.
- Order-wise yarn requirement planning based on approved quality and production assumptions.

Party, supplier and accounting operations

- Party and supplier ledgers with debit, credit, receipt, payment and outstanding balances.
- Invoices, receipts, payment allocations and accounting exports.
- Deeper financial workflows beyond the operational receivables included in Option B.

Advanced platform administration and governance

- Expanded tenant administration, subscription oversight, usage visibility and operational support controls.
- Advanced audit registry for critical security, financial, material and correction events.
- Security lockdown, session revocation and controlled tenant/user restrictions.
- Compliance and data-governance case-management workflows.

Advanced analytics and intelligence

- Expanded business intelligence dashboards for production, profitability, utilisation, receivables, payroll and stock trends.
- Cross-factory benchmarking using privacy-safe aggregated data where approved.
- Predictive production planning, deadline-risk indicators, output forecasts and capacity insights, subject to sufficient historical data.

Native mobile applications

- Native Android and/or iOS applications for selected owner and supervisor workflows.
- Mobile-specific UX, push notifications and app-store deployment where separately scoped.
- Offline or low-connectivity capabilities may be assessed separately based on required workflows.

Loom and IoT integrations

- Integration with loom sensors, production counters, gateways or other supported hardware.
- Automated metre capture, machine status and telemetry where technically feasible.

- Final scope depends on hardware manufacturer, communication protocol, API/SDK availability and factory connectivity.

6.2 Option C Proposed Team and Effort

Because Option C consists of independently selectable future modules, the final team structure and effort will depend on the modules commissioned.

Role	Seniority	Count	Allocation
Project Manager / Business Analyst	Senior	1	Part-time
Technical Lead / Solution Architect	Senior	1	Part-time
UX/UI Designer	Mid-Senior	1	As required
Frontend Engineers	Senior	1-2	Module dependent
Backend Engineers	Senior	1-3	Module dependent
QA Engineers	Mid-Senior	1-2	Module dependent
DevOps / Cloud Engineer	Senior	1	As required
Mobile / Data / IoT Specialist	Senior	As required	Specialist modules only

6.3 Option C Timeline and Milestones

Milestone	Indicative period	Primary deliverable
C1. Module-specific discovery	Weeks 1-3	Validated workflows, assumptions, integrations and acceptance criteria
C2. UX/UI and architecture extension	Weeks 2-5	Designs, data model and integration approach
C3. Module implementation	Weeks 10-12	Selected optional module
C4. QA and integration validation	Weeks 18-20	Party-backed and make-to-stock production contexts
C5. UAT and production release	Final 2-4 weeks	UAT, deployment, documentation and handover

6.4 Option C Commercial Approach

Option C modules will be quoted separately based on the specific functionality selected.

The commercial approach may be:

- Fixed price after bounded module-specific discovery.
- Clearly bounded price range where residual uncertainty remains.
- Time-and-material engagement for predictive, experimental or hardware-dependent scope.

The indicative effort ranges are intended for budgetary planning and will be confirmed against the selected module scope, integrations and acceptance criteria.

6.5 Option C Assumptions

- Option B platform foundations are assumed available where relevant.
- Existing tenancy, authentication, roles, audit and deployment components may be reused where technically suitable.
- Accounting, tax, inventory and textile business rules will be supplied or validated by the client.
- Predictive features depend on sufficient historical data quality and quantity.
- IoT pricing requires hardware, protocol and API/SDK details.
- Native mobile applications require separate mobile UX, QA and app-store release activities.
- Third-party licences, hardware, provider fees and external approvals are excluded unless explicitly stated.

6.6 Option C Exclusions

Unless separately scoped, Option C does not automatically include:

- Complete statutory accounting or GST return filing.
- Government-portal submission automation.
- Hardware procurement or physical sensor installation.
- Guaranteed predictive or AI accuracy.
- Large-scale historical data cleansing or migration.
- Third-party licence and provider fees.
- 24x7 managed operations.

7. Proposed Technical Architecture


Layer	Recommended approach
Frontend	React / Next.js responsive PWA with mobile-first production workflows
Backend	Node.js / NestJS-style modular service architecture, subject to final technical sign-off
Database	PostgreSQL relational database for transactional consistency, reporting and constraints

PROJECT SCOPE

Layer	Recommended approach
Async processing	Queue-backed jobs where needed for messaging, webhooks, PDFs and retryable background work
Storage	Client-owned cloud object storage for generated documents and appropriate assets
Hosting	Client-owned AWS, Azure or GCP account, final provider selected during mobilisation
Observability	Structured logs, production monitoring/error tracking, webhook/payment/messaging diagnostics and alerts
Source control	Client-owned Git repository from project commencement
Environments	Separate development, QA/staging and production configurations and credentials

7.1 Proposed Weavly Application Architecture


The following high-level architecture illustrates our proposed modular approach for delivering Weavly as a secure, scalable, multi-tenant SaaS platform. It connects the Owner application, Supervisor PWA and Platform Administration interface with dedicated business services for textile estimation, production, inventory, dispatch, commercials, payroll, billing and operational reporting.

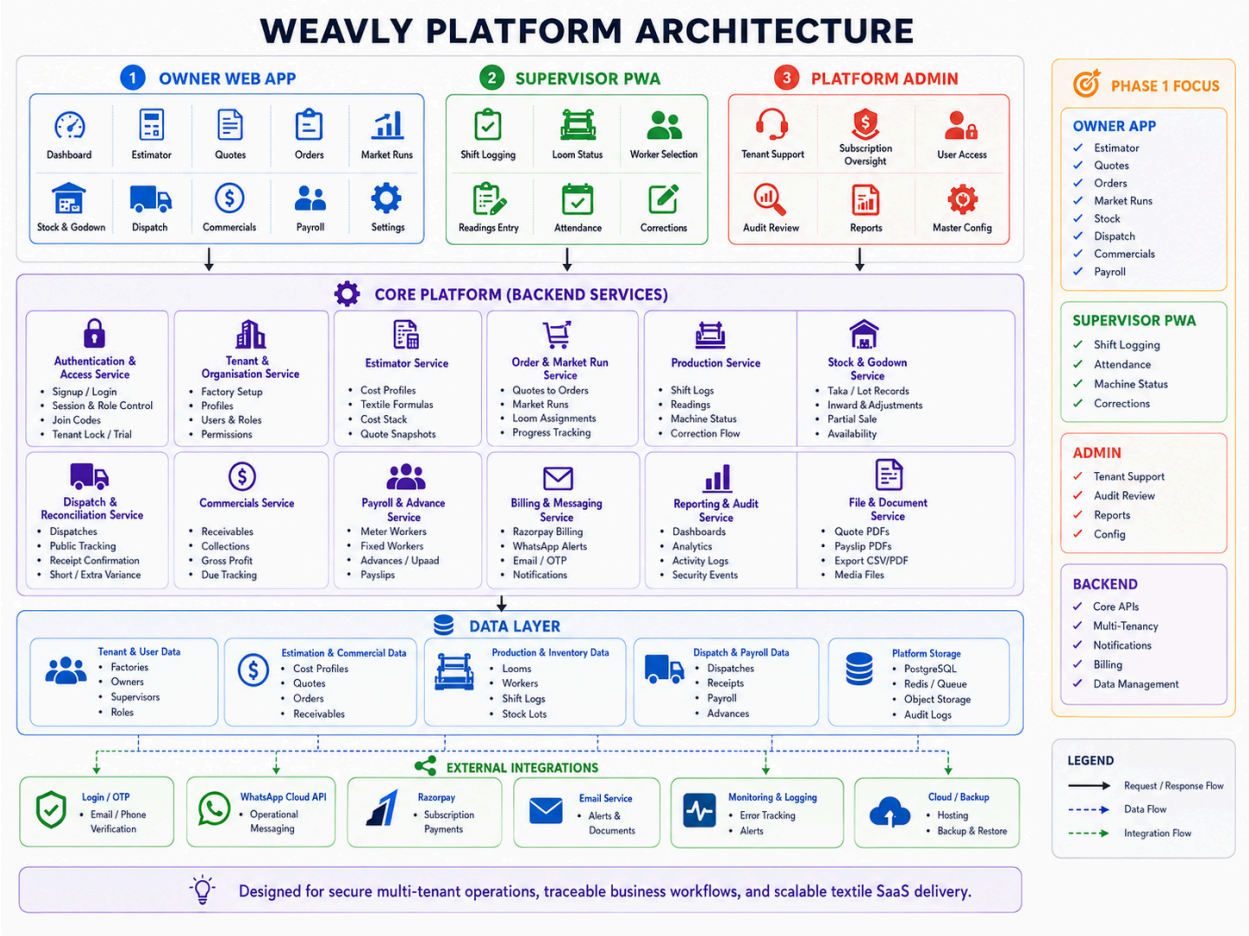

https://drive.google.com/file/d/1dndEnhnGXaGA-uTtxf-1EK-LtTw6AVyV/view?usp=sharing

7.2 Proposed DevOps, Cloud Deployment and Observability Architecture

The following architecture illustrates Narola Infotech's proposed approach to secure software delivery, environment separation, CI/CD automation, scalable cloud infrastructure, monitoring, logging, backup and disaster recovery. The final infrastructure configuration will be right-sized during discovery based on the selected cloud provider, agreed availability targets, projected usage volumes and infrastructure budget.

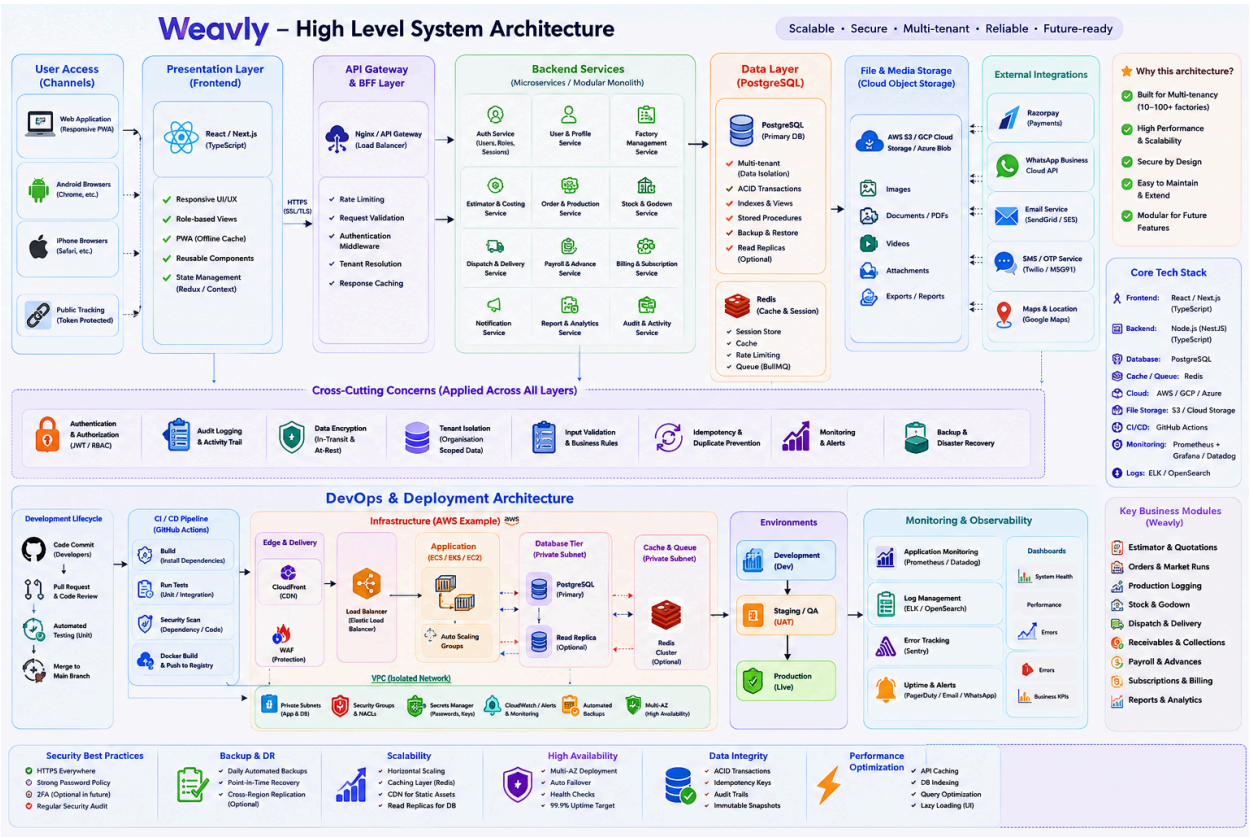

https://drive.google.com/file/d/1MG3j9PFPJgBmHvH7t6Ht0HHEf6umDLUu/view?usp=sharing

8. Security, Tenant Isolation and Data Integrity

- Organisation scoping on protected reads and writes, with application-level authorisation and database-level safeguards appropriate to the selected design.
- Server-side validation for material and financial operations, client-side validation remains supplementary.
- Role enforcement for owner, supervisor, platform administrator and public recipient/buyer flows.
- Rate limits and abuse controls for login, join/access codes, public tracking and sensitive APIs.
- Secrets outside source code, separate environment credentials and least-privilege access.
- Atomic database transactions and controlled state transitions where partial completion would create inconsistency.

- Idempotent handling for duplicate clicks, network retries, payment webhooks, stock inward, dispatch, receivables and settlements.
- Audit/event logging for critical security, material, financial, correction and reversal events.
- Backup, restoration and incident-response approach documented before production handover.

9. QA and Acceptance Strategy

- Unit tests for estimator formulas, quantity arithmetic, payroll and other deterministic business logic.
- Integration tests for database/service operations, tenant isolation, state transitions, webhooks and idempotency.
- End-to-end browser tests for principal owner and supervisor workflows.
- Manual mobile/responsive, usability and exploratory edge-case testing.
- Security testing for logged-out, wrong-role and cross-tenant access attempts.
- Performance smoke tests using representative record volumes agreed during discovery.
- UAT against client-supplied textile examples and pilot scenarios.
- No unresolved blocker or critical defect at production handover unless expressly accepted in writing.

10. Mandatory Acceptance Journeys

- Fresh owner account -> onboarding -> machines/workers/godown/party/quality -> usable estimator.
- Estimator -> quote -> accepted quote -> order -> loom assignment -> supervisor log -> owner progress -> payroll earning.
- Estimator market mode -> market run -> loom assignment -> supervisor log -> stock inward -> partial stock sale -> remaining quantity.
- Stock/order sale -> dispatch -> public receipt -> shortage/extra reconciliation -> commercials receivable.
- Worker advance -> payroll preview -> capped deduction -> settlement -> payslip -> remaining advance balance.
- Wrong-role, logged-out and second-tenant attempts against protected routes and APIs.
- Refresh/re-login after each critical write, including duplicate-click and network-retry checks.

11. Infrastructure and Third-Party Costs

Service	Initial budgetary assumption
Cloud hosting + managed database	Approximately INR 35,000-70,000 per month for production plus staging at early year-one scale, final cost depends on provider and architecture
Storage and backups	Approximately INR 5,000-15,000 per month depending on retention and document volume
Monitoring / error tracking	Free-to-paid tier depending on event volume, budget INR 0-15,000 per month initially
Email service	Usage-based, normally low at initial scale
WhatsApp Business / Cloud API	Usage-based and provider-controlled, charged directly to client account
Razorpay / payment gateway	Provider transaction fees apply, paid directly by client

External approval, KYC, business verification and provider onboarding time are third-party dependencies and excluded from Narola-controlled delivery commitments. Narola integration development and reasonable submission support are included where scoped.

12. Warranty and Post-Launch Support

Item	Proposal
Included defect warranty	3 months from production acceptance
Critical severity initial response target	Within 4 business hours during Narola business hours
High severity initial response target	Within 1 business day
Medium severity initial response target	Within 2 business days
Low severity initial response target	Within 3 business days
Post-warranty annual maintenance option	15% of implementation value per year, scope and SLA to be agreed
Alternative support model	Time and material at INR 1,500 per engineering hour, subject to resource availability
Change request rate	INR 1,500 per engineering hour unless separately quoted as fixed-price scope

Warranty covers defects where delivered functionality does not conform to the accepted scope. New functionality, changed business rules, new integrations, third-party API changes, new statutory requirements and unauthorised external changes are excluded from defect warranty.

13. Top Five Delivery Risks and Mitigation

Risk	Control / mitigation
Textile formula correctness	Client-defined formulas and worked examples, deterministic implementation, automated unit tests, calculation explanation, UAT against expected outputs.
Cross-module data integrity	Atomic transactions, historical snapshots, database constraints, reconciliation rules and integration tests across production, stock, dispatch, commercials and payroll.
Multi-tenant data exposure	Organisation scoping, application/database controls, server-side authorisation and dedicated cross-tenant tests.
Business-rule ambiguity discovered during implementation	Bounded discovery, signed scope baseline, decision log, explicit assumptions and formal change control.

Risk	Control / mitigation
Third-party approval delay	Start account onboarding early, use test/sandbox environments where available, complete integration work in parallel and separate provider approval time from agency-controlled delivery.

14. Source Code, IP and Handover

- Custom source code, client-specific database schema, designs, documentation and test assets are assigned to the client upon payment according to the final contract.
- Client-owned Git repository access from project commencement.
- Disclosure of pre-existing agency frameworks, commercial components and open-source dependencies before use where material.
- Development, QA/staging and production environments with documented configuration.
- Deployment pipeline, monitoring, logging, backup and restore documentation.
- Admin/user documentation and knowledge-transfer sessions.
- Production cloud, domain, payment gateway, messaging and monitoring accounts should be client-owned wherever practical.

15. Relevant Narola Infotech Experience

We recommend presenting experience by technical similarity rather than forcing an exact textile-industry match. The following examples are suitable for the final client package:


Project	Relevance to Weavly
GeminiSmart - Cloud CMMS SaaS platform	Asset and maintenance operations, work orders, reporting, compliance, mobile field operations and SaaS-style workflows. https://www.geminismart.org/
Biocon - Digital enterprise engagement	Relevant enterprise-scale delivery experience for a leading life-sciences organisation, public Narola case study available https://www.narolainfotech.com/case-study/biocon/

Few more relevant experiences we have: those client contacts should only be shared after obtaining permission. To avoid misrepresenting private contact details, the proposal states that comparable client references are available upon request and subject to client consent.

16. Production-Readiness Declaration

The quoted Option A and Option B estimates are for production-ready commercial systems, not prototypes or proof-of-concept demonstrations. The baseline includes discovery, UX/UI, architecture, frontend, backend, database, security, QA, deployment, monitoring, backup approach, documentation, knowledge transfer, source-code handover and warranty, subject to the stated assumptions and exclusions.

Our Agile Development Process

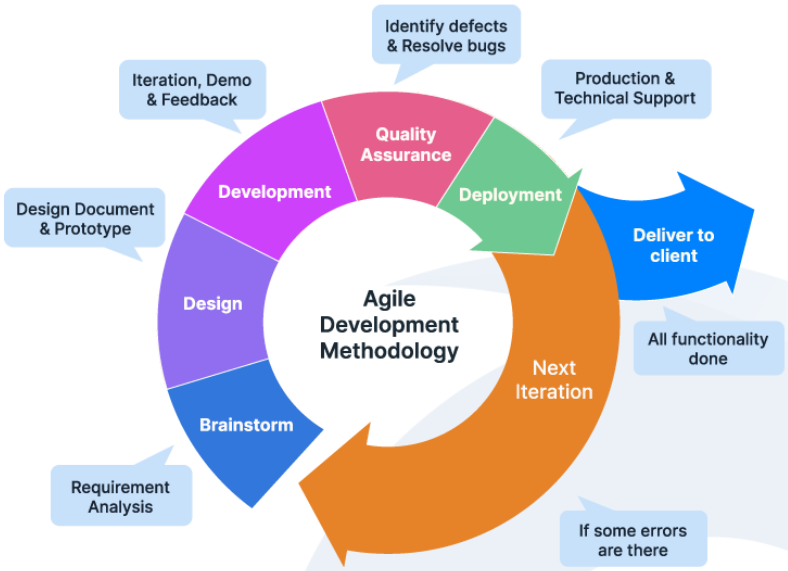

We delicately follow the Agile + iterative approach to work on each of our projects. We ensure the deliverables remain seamless, flawless and are completed within the set time frame.

Our agile methodology aims to deliver the right product with incremental and frequent delivery of small chunks of functionality through small cross-functional self-organizing teams, enabling frequent customer feedback and course correction as needed. Requirements, plans, and results are evaluated continuously, so our agile teams have a natural mechanism for responding to change quickly.

Evaluation + Measurements of Success

To ensure transparency and keep you informed, the following practices will be implemented throughout the development period:

1. **Daily Status Update**: At the end of each day, a comprehensive email will be sent summarizing the completed work and ongoing tasks. This will provide a clear overview of the progress made.
2. **Progressive Builds**: Scheduled intervals will be established for sending progressive builds tailored to the respective platforms. These builds will showcase the evolving development and enable you to track the project's advancement.
3. **Task Limitations and Alternatives**: In the event that backend tasks or other factors hinder the generation of builds, screenshots or videos will be shared as relevant alternatives.

By implementing these practices, we aim to foster transparency, keep you informed, and provide a visual representation of the project's development progress.

Project Investment & Timeline Analysis

Commercial Summary

Option	Scope	Budgetary fixed-price estimate	Indicative timeline
Option A	Standalone Estimator Product	Estimate Hours: Approx 2200 Hourly rate: 1500 INR per hour Total: INR 33,00,000 + applicable GST	Approximately 24-26 weeks
Option B	Full Weavly Suite including Option A	Estimate Hours: Approx 8500 Hourly rate: 1500 INR per hour Total: INR 1,27,50,000 + applicable GST	Approximately 48-52 weeks
Option C	Optional future ERP, inventory, governance, analytics, mobile and IoT modules	To be discussed based on selected scope	To be discussed

Commercial note: The above values are indicative budgetary estimates based on the RFP, client clarifications, currently available information and the assumptions stated in this proposal. Final pricing will be confirmed against the mutually accepted scope baseline. Any material scope changes, new integrations, statutory or compliance requirements, native mobile applications, IoT integrations or large-scale data migration will be handled through formal change control or separately priced under Option C.

Assumptions and Considerations


- Greenfield delivery: no existing source code, database schema, design system or automated test suite is assumed reusable.
- The client supplies textile formulas, terminology, representative worked examples and expected outputs for acceptance testing.
- Initial launch language is English, architecture permits future Gujarati/Hindi localisation but translations are excluded unless separately agreed.
- Baseline delivery is a responsive web application/PWA, native mobile apps are Option C.
- A taka has no globally fixed metre value, actual recorded metres govern stock calculations while taka count is retained.
- Client review and approval cycles are assumed within five business days unless otherwise agreed.
- Material changes after scope-baseline approval follow formal change control.
- Client-owned accounts for cloud, Razorpay, WhatsApp, email and monitoring can be opened in parallel after commencement.
- Third-party verification and approval delays remain outside Narola-controlled delivery commitments.

- Planning volumes follow the client-provided scale assumptions and are not contractual usage caps.
- Large historical data migration is excluded until source data is assessed.
- No hardware/IoT integration or automated loom meter capture is included in baseline scope.

Exclusions:

- Native iOS or Android applications.
- Complete statutory accounting, GST return filing, general ledger or Tally replacement.
- Full supplier accounting and purchase-management ERP.
- Deep yarn-lot, beam-card, yarn-consumption and raw-material inventory management.
- Advanced logistics routing, transporter marketplace or GPS tracking.
- Hardware/IoT connection to loom sensors or automatic meter capture.
- Custom payroll statutory filing or government-portal submission automation.
- Large-scale historical data migration unless separately estimated after assessment.
- 24x7 managed operations beyond the quoted warranty/support arrangement.

Team Structure

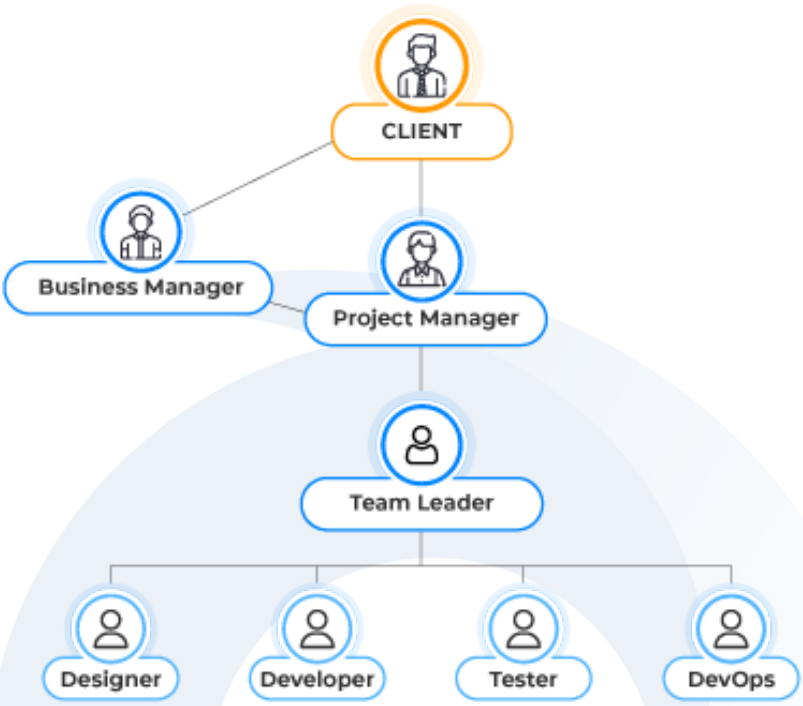

Your Accountabilities & Responsibilities

Timely Feedback and Communication: As a part of the process, the daily comprehensive work update report will be sent, summarizing the completed work and ongoing tasks with Progressive Builds Scheduled intervals, showcasing the evolving development and enabling tracking of the project's advancement. Timely feedback on daily work updates is expected from the clients with topmost priority to ensure smooth project execution. Additionally, timely communication is crucial for the timely completion of the work. Responsiveness to queries or communication raised by the team within 24-48 working hours is expected from the clients. Failure to provide timely feedback may necessitate project resource reallocation, redoing the work or potential impacts on the deadline and cost.

Maintaining Team Alignment During Project Holds: In the event that unexpected circumstances arise, causing the project to be put on hold for more than a week or two, clients are responsible for informing the development team. This ensures transparency and helps the team manage resources effectively.

Provision of necessary information, resources, and guidance: The necessary access credentials, documentation, and relevant information required for integration with existing systems or utilization of external APIs are expected to be provided by the clients. The responsibility lies with the clients to provide the actual data or sample data to be used within the software, including data structure, data sources, and specific requirements related to data management and migration. If there are specific design assets such as logos, images, or branding guidelines, it is expected that the clients provide them to ensure alignment with their visual expectations. Furthermore, the development team should be informed by the clients about any legal or compliance requirements that need to be addressed during the software development process, including privacy regulations, data protection laws, or industry-specific compliance standards.

WHY WE'RE BEST FIT

Corporate Value Proposition


- Patience with Clients
- Diversified Industry Portfolio
- Dedication to Client's Vision & Empowerment
- Proactive in Suggesting Best Practice Solutions
- Prioritizes Personal Privacy and Data Security
- Customer-Centric, Collaborative and Communicative Approach

Our Statistics



Our Public Listed Fortune Clients



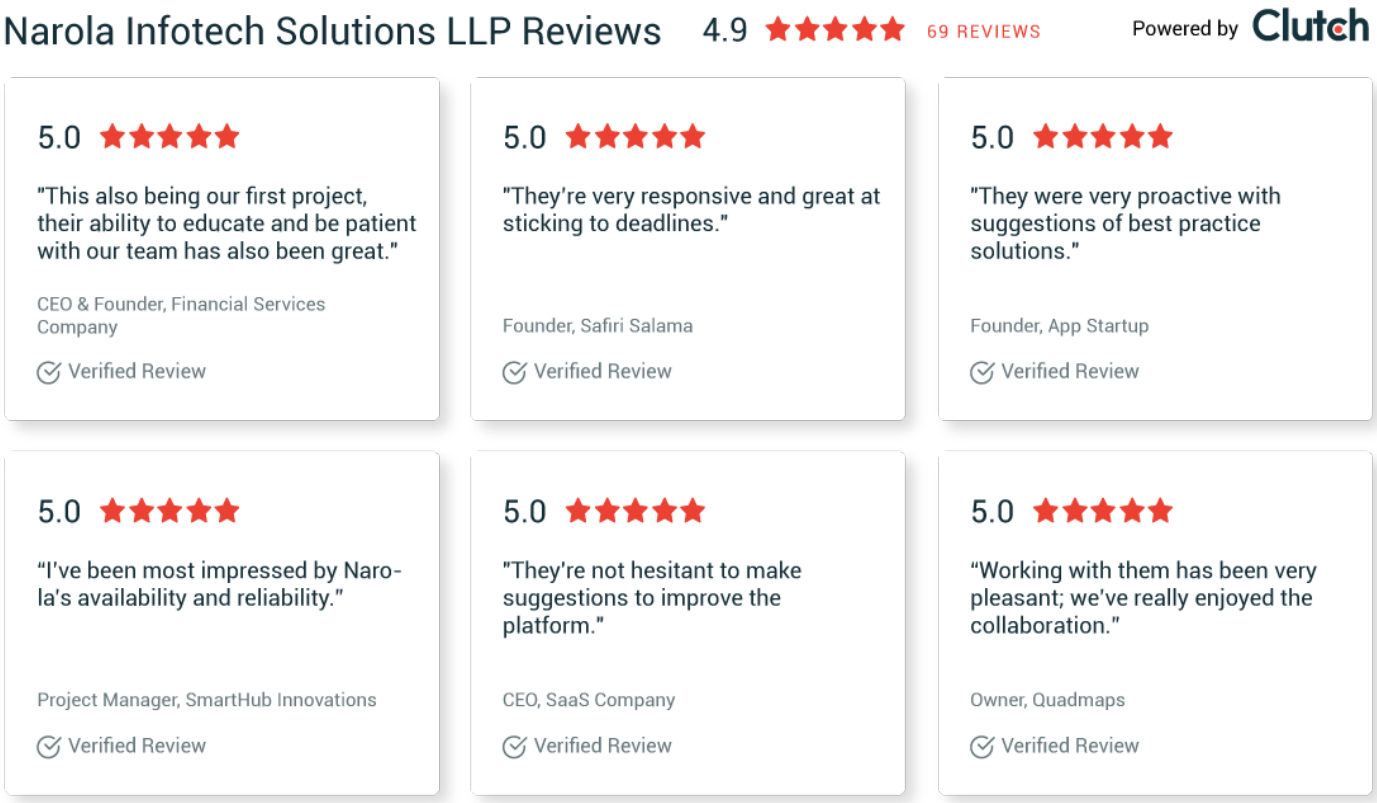

Terms and Condition

- **Timeline:** The provided timeline is subject to change based on resource availability during the hiring process. The duration may be extended or shortened depending on factors such as project complexity, module dependencies, and resource availability, with the possibility of completing the project earlier at no additional cost.
- **Change Management Process:** During the development phase, the team will provide a daily work report and build to ensure the project progresses smoothly. It is expected that you shall provide feedback within the defined scope of work provided, in order to avoid any additional User Acceptance Testing (UAT) work. Any feedback provided by you that falls outside the scope of work will be considered through the change management process. The Change Management process will handle any changes in scope that may arise during the project execution. The features identified as part of the current scope are clearly outlined in the task breakdown document. You will be informed of any associated costs or timeline adjustments that may result from such additions.
- **Payment Obligations:** Both the buyer and the service provider agree to fulfill their payment obligations as per the agreed amount (Price) for the software project.
- **Limited Liability:** In the event of non-payment or any issues arising from this agreement, the legal responsibility of either party towards each other will be restricted to the agreed amount (Price).
- **Excluded Losses:** While the parties have limited liability, there are certain types of losses that cannot be excluded by law. However, except for those specific cases, neither party will be held accountable for any indirect or consequential losses or damages. This includes but is not limited to loss of profits, goodwill, business, data, or any other similar types of losses.
- **Non-poaching:** The client must not, either directly or indirectly, knowingly engage in actions that encourage or try to persuade any employee, contractor, consultant, principal, agent, or representative of the Service Provider and its Affiliates who are involved in discussions or negotiations to end their relationship or stop working with the Service Provider and its Affiliates. Additionally, the client must not attempt to recruit or hire any employee of the Service Provider and its Affiliates for their own employment or assist others in doing so.
- **Source Code Delivery and Backup:** Narola Infotech will deliver the source code to the client upon the successful completion of each milestone. It is the client's responsibility to thoroughly verify the provided source code. Additionally, the client is required to maintain a backup of the source code for their records and security. Upon completion of the project, Narola Infotech will retain a backup of the source code for a period of at least 3 months only after the project's warranty period concludes.
- **Development Environment (Server) Provision:** The client is responsible for providing the necessary development environment (server infrastructure), at the project's outset. In the event that the client is unable to arrange a server initially, Narola Infotech will facilitate development on their own demo server. Throughout the project's development phase, Narola Infotech will maintain the system on their demo server, ensuring it remains live and accessible until the project reaches completion. However, if the project experiences a hold period lasting one month or more, Narola Infotech will take the necessary security measures and temporarily take down the system from their demo server. Narola Infotech is not liable to keep the server always up for client's demo.
